




CONSTRUCTION REPORT May 2020

West Campus Roundabout

- Gomez Construction is the selected contractor
- Construction started on May 18th 2020
- Completion scheduled for August 2020

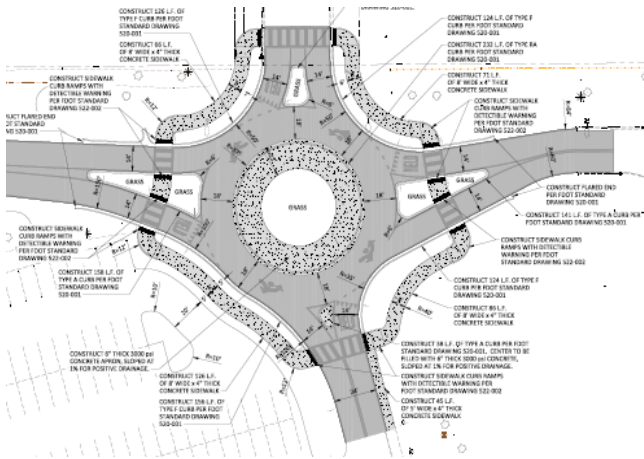

Osceola Building 1 Second Floor Renovation

- Project scope needed to be expanded to include a portion of the first floor, which allowed the newly desired multi-purpose room to be code compliant (Could not be built on the second floor without adding another exit stair from the building).
- Revised 95% Construction Documents are due June 1.
- Oelrich Construction is providing Pre-Construction Management Services. An updated construction cost will be submitted in June.
